



DEPARTMENT OF THE ARMY  
CORPS OF ENGINEERS, PORTLAND DISTRICT  
BONNEVILLE LOCK AND DAM PROJECT  
PO BOX 150  
CASCADE LOCKS OR 97014-0150

CENWP-OD-B

30 July 2014

MEMORANDUM FOR Biologist, Operations Division (CENWP-OD)

SUBJECT: Bonneville Project, Fishway and Fish Activities for Week 30 of 2014, which covers the period from 20 – 26 July 2014

**1. OPERATION SUMMARY:**

a. Daily average river flows ranged from 172.9 to 205.8 kcfs. Daily average project tailwater ranged from 15.1' to 17.0' msl. Daily average powerhouse forebay elevation ranged from 74.8' to 75.5' msl. Daily average water temperatures remained at 69° all week. Secchi disk measurements remained at 7.0' or greater all week.

b. Spill Bays 01 and 18 provide attraction flow for Cascades Island and B-branch, respectively. Summer spill operations congruent with FPP section 2.2.3 took effect on 16 June. Daily spill ranged from 90.7 to 100.5 kcfs this week.

c. Unit Operation. Split flow powerhouse operations went into effect on 23 June and ceased on 9 July.

(1) Table 1. Unit Outages.

Unit	OOS Date	RTS Date	Reason
1	0037 on 21 Jul		
2	0854 on 07 Jul	---	5-yr overhaul
5-8	0725 on 23 Jul	1539 on 24 Jul	230 KV line BPA maint.
11	0900 on 09 Sep 2012	---	High thrust bearing temps

d. Fish Units. Second Powerhouse fish units provide attraction flow for the Washington Shore (WS) fish ladder. The units may be placed on standby, as necessary, during nighttime hours to float debris. Gatewell drawdowns are measured on Tuesdays and more frequently as needed.

(1) Table 2. Fish unit drawdowns, in feet.

Date	F1	F2
7/20	0.4	0.9
7/21	0.5	0.5
7/22	0.5	0.5
7/23	0.3	0.2
7/24	0.9	0.5
7/25	0.2	0.6
7/26	0.8	0.7

**2. ACTIVITIES:**


- a. Auxiliary Water System Closures. No closures occurred this week.
- b. STS/VBS inspections. No inspections occurred this week.
- c. Dewatering and Fish Salvage. No dewatering or salvage activities occurred this week.

**3. RESEARCH:**


a. Avian Monitoring. Avian abundance is documented daily during fishway inspections by a Project Biologist. Due to low bird populations at the dam during winter months, bird numbers are recorded 7 days a week between the dates of 01 April and 31 October. Avian monitoring occurs as often as possible outside of these dates and during the non-fish passage season.

(1) Hazing Effectiveness. Avian hazing continues to be effective and abundance continues to be low. This is the last full week of avian hazing as USDA hazing activities ends on the 31<sup>st</sup> of July.

(2) Chart 1. Avian predation by day.

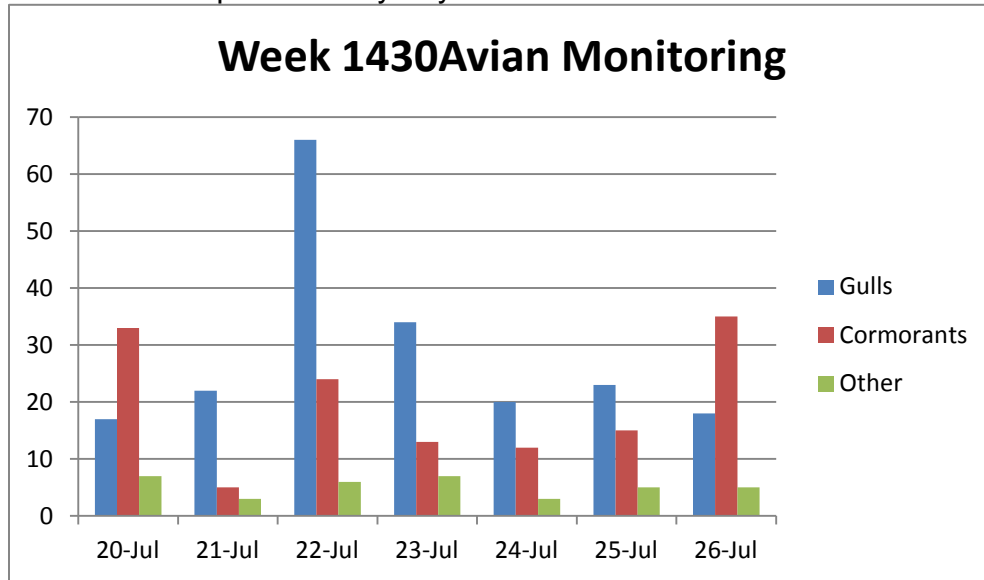

(3) Chart 2. Avian predation by zone.

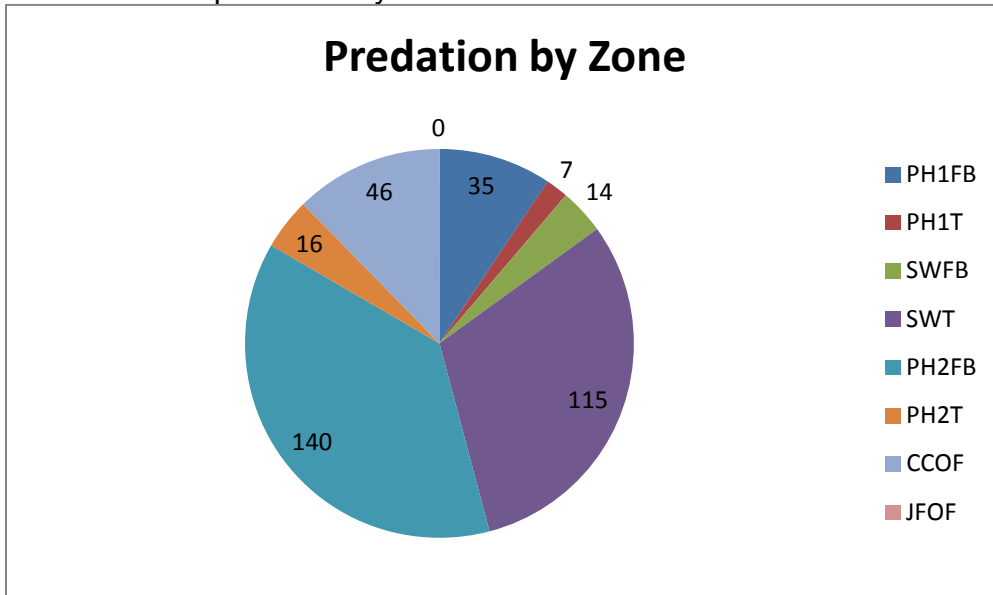

(4) Table 3. Tailrace Counts of Foraging Piscivorous Birds.

Date	Time	Gulls	Cormorants	Terns
7/20	0930	6	2	0
7/21	0800	19	5	0
7/22	1230	65	2	0
7/23	0830	26	2	0
7/24	0930	14	0	0
7/25	1000	21	1	0
7/26	1100	12	0	0

(5) Figure 1. Avian Predation Map.



b. CRITFC – AFF. Sampling continues.

c. NOAA Fisheries. An impedance counter is currently being tested at the WA Shore AWS LPS. Lamprey trapping at the AFF in conjunction with University of Idaho continues. Lamprey structure design testing in the FERL continues.

d. Normandeau – Fish Counting. Visual counting continues.

e. PSMFC – Smolt Monitoring Program. Juvenile fish condition and index monitoring continues. No research fish were collected this week. Fallbacks recorded crossing the separator bars this reporting week: 6 salmon. Results of this week's Gas Bubble Trauma (GBT) examinations: 200 subyearling Chinook examined, with none exhibiting GBT symptoms. More details can be found on the [FPC web page](#).

f. University of Idaho – AFF. USACE-funded adult salmonid sampling continues.

Lamprey trapping at the AFF in conjunction with NOAA continues. IR camera monitoring in the Bradford Island serpentine section began on 16 July.

g. USDA - Avian Hazing. Avian hazing will conclude on 31 July.

h. USFWS - Fish Health. When possible, all fish mortalities are being held for inclusion in the National Wild Fish Health Survey. CRITFC is also testing lamprey mortalities for contaminants in conjunction with USFWS.

**4. FISHWAYS:**

a. Project biologists inspected 20 – 26 July.

b. Fish Passage Plan Observations.

(1) Table 4. FPP Out of Criteria items.

Date	Location	FPP Items	Cause	Response
<b>BRADFORD ISLAND</b>				
7/25-26	PH1CC	N-Diff < 1.0'	Unknown	None
<b>CASCADES ISLAND – Nothing to report</b>				
<b>WASHINGTON SHORE</b>				
7/22	SUE/SDE	Entrance diff < 1.0'	Unknown	None

(2) PH2CC diffuser A2 is stuck closed, and the gate to B3 has been removed for repairs. Diffusers B7 and B8 have been closed until repairs to their diffuser motors can be performed. The next possible time period will be 2014/15 winter maintenance.


(3) Spill bay 17 experienced a hoist brake failure on 11 March. The gate is currently dogged off at 2.9 ft.

c. Fishway Temperatures. Temperatures are taken from 01 March through 30 November. Forebay temperatures can be found [online](#).

(1) Table 5. Daily Average Temperature in Degree Fahrenheit (°F).

Date	Fishways				Forebay	Lamprey systems			
	Brad. Is.	AFF	SMF	WA shore		BI LPS	CI LPS	WA LPS	NDE LPS
7/20	68.7	68.5	69.3	68.4	69.4	69.2	68.7	68.1	68.2
7/21	68.6	68.4	69.3	68.4	69.3	69.2	68.7	68.1	68.2
7/22	68.7	68.5	69.4	68.4	69.3	69.2	68.7	68.1	68.2
7/23	68.5	68.4	69.3	68.2	69.4	69.0	68.4	67.8	67.8
7/24	67.8	67.6	68.5	67.5	69.2	68.3	67.8	67.2	67.2
7/25	67.9	67.7	68.5	67.6	68.5	68.4	67.9	67.3	67.4
7/26	68.3	68.0	68.8	67.9	68.6	68.9	68.3	67.7	67.9

(2) Chart 3. Daily Average Temperature in Degree Fahrenheit (°F).

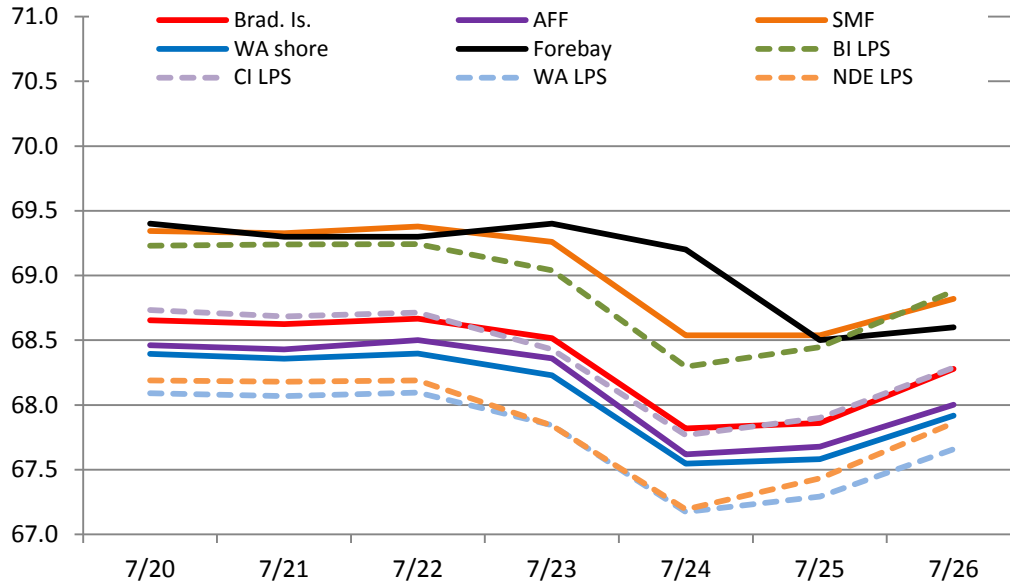

d. Zebra Mussel Monitoring. No signs of colonization were observed this reporting week.

e. Adult Fishways.

(1) Calibration was checked on 25 July. All sensors were within criteria.

(2) 11 of 12 floating orifice gates (FOGs) are installed; one gate is out for maintenance. FOG SLEDs are installed.

(3) All SLEDs are removed.

f. Juvenile Fishways.

(1) The south end gate of the Ice and Trash Sluiceway (ITS) remains removed for ongoing repairs. Plating has been placed over the bottom of the guide slot to minimize fish impacts. The ITS will need to be closed for reinstallation once repairs are complete.

(2) The DSM remains in service.

(3) The hydro-cannon remains in service.

CENWP-OD-B

SUBJECT: Bonneville Project, Fishway and Fish Activities for Week 29 of 2014, which covers the period from 13 – 19 July 2014

(4) The B2CC remains open.

(5) The B2CC avian array was removed on 09 – 10 October 2013 to facilitate the WA Shore LFS repairs. The anchor line was replaced on 27 March, and the array will be reinstalled after spill season. The PH1, PH2, and spillway avian arrays remain intact.

g. Lamprey Fishways.

(1) The BI LPS, CI LPS, NDE LPS, and WA Shore AWS LPS remain in service.

**5. CONSTRUCTION:** Nothing to report.

**6. HAZMAT, SPILLS AND CLEANUP:** Nothing to report.

**7. TELETYPES CURRENTLY IN EFFECT:**

a. A teletype sent on 17 March states that effective 17 March at 0800 hours, operate the B2CC continuously through 31 August at 2400.

b. A teletype sent on 30 June updates the spill caps and lack of load conditions to be used from 11 June through 31 August.

c. A teletype sent on 13 June requests BON forebay be maintained from 74.5' to 76.5' hard constraint and from 75.5' to 76.5' soft constraint from 1400 – 2000 on 08 August and from 1500 – 2200 on 09 August so that sailboats can be placed and removed from the water. The request may be cancelled at 1500 on 08 August if high winds occur.

d. A teletype sent on 13 June lists the BON summer spill requirements in effect from 0430 on 16 June until 2400 on 31 August.

e. A teletype sent on 18 July requests that the BON pool operate within a 1.5' band, hard constraint, from 0600 on 21 July until 1800 on 25 July for treaty fisheries. A similar teletype sent on 24 July requests the same operation from 0600 on 28 July until 1800 on 31 July.

f. A teletype sent on 18 July requests that from 1100 – 1800 daily, BON forebay be maintained no lower than 74.0' on 25 July and 74.5' on 26 – 27 July, soft constraint, for a kite boarding event.

CENWP-OD-B

SUBJECT: Bonneville Project, Fishway and Fish Activities for Week 29 of 2014, which covers the period from 13 – 19 July 2014

g. A teletype send on 24 July requests that the BON forebay be maintained at 74.0-76.5', hard constraint; and 75.0-76.5', soft constraint for the berthing of keel boats at Stevenson from 1600 on 01 August until 1100 on 02 August, and from 1600 on 02 August until 1100 on 03 August.

JERRY A. CARROLL  
Operations Manager  
Bonneville Project
