

FISHWAY STATUS REPORT

Date: 3/30/2014
Inspection Period: 3/23 thru 3/29/2014

All JD Fishways are inspected twice per day during fish season, March. 1 - Nov. 31
 Frequent monitoring of the PLC displays in SMF Fisheries Office as necessary.

	JOHN DAY DAM	
	JD/WC Project-Fisheries P.O. Box 823 Rufus, Oregon 97050 Phone: 541-506-7860	

John Day Dam	Inspections	Criteria	Total Number of Inspections: 14	Temperature: 43.4 F
	Out of Criteria	Limit		Secchi: 2.6 Ft.
NORTH FISHWAY			Meeting the optimal FPP criteria; 4 out 6 AWS pumps available/in service	
Exit differential	0	≤ 0.5'		
Exit Control weirs	0	High setting	High setting is normal for JDN	
Count station differential	0	≤ 0.3'		
Weir crest depth	0	1.0' ± 0.1'		
Diffuser Sluice Gate (D2.1-D2.8)	0	per PLC		
Entrance differential	0	1.0' - 2.0'	AVG 1.5	
SOUTH FISHWAY			In regular service with all three AWS turbines since 3/11.	
Exit differential	0	≤ 0.5'		
Exit Control weirs	0	MID setting	MID is normal for JDS	
Count station differential	0	≤ 0.3'		
Weir crest depth	0	1.0' ± 0.1'		
South entrance differential	0	1.0' - 2.0'	AVG 1.3	
Entrance weir SE1	0	depth (≥ 8')	AVG 8.6	
Collection channel velocity	0	1.5 - 4 fps	AVG 3.1	
Bay 1 differential	0	1.0' - 2.0'	AVG 1.7	
N. Entrance PH(Bay 19)differential	0	1.0' - 2.0'	AVG 1.6	
Entrance weir NE1	0	depth (≥ 8')	AVG 11.0	
Entrance weir NE2	0	depth (≥ 8')	AVG 10.9	
JUVENILE PASSAGE				
Forebay/bypass conduit differential	N/A	4.0' - 5.0'	AVG 4.5	
Submersible traveling screens	N/A	visual inspect	Underwater camera inspections occur the third week of each month.	
Turbine trashrack drawdown	N/A	<1.5', wkly	JD Structural raking of MU trashracks occurs the last week of each month.	
Vert barrier screen drawdown	N/A	<1.5', wkly	JD Fisheries crew performs frequent gate wells' drawdowns depending on river debris.	
Spill volume	N/A	n/a		
Spill pattern	N/A	n/a		
Turbine Unit Priority	N/A	per FPP		
Turbine 1% Efficiency	N/A	per FPP		

SMOLT MONITORING FACILITY

Operation: SMF was watered up on 3/25 and then switched to sampling mode on 3/31 AM. First sample was processed by PSMFC on 4/1. PDS screen cleaner in regular service with only occasional stops/ glitches, which are being fixed by JD Electrical crew immediately.

Debris: N/A

Maintenance:

Minor PDS screen cleaners' calibrations by JD Electrical crew underway.

Brand new, replacement CCTV system working great and displaying much improved view of F/D separator.

Research:

Battelle setting up for collections, tagging and holding of juvenile salmonids at JD SMF. The first collection/tagging is expected in late April.

Fallbacks: AVG: 0 MAX: 0 MIN: 0

OTHER ISSUES:

JOHN DAY

Birds: See Avian tabs.

122 primary avian lines are properly installed. Three primary and two filler lines are missing; one attaching to Navlock broke on 1/10/14. JD Maintenance had attempted to create a plan for re-installation of all missing lines, but it isn't possible due to the lack of O&M manual. District has been informed. JD Engineering is attempting to contract out the re-installation of three missing primary lines before 10 April deadline.

Operations:

JD North Fishway is in regular service and meeting the optimal FPP criteria.

JD South Fishway in regular service since 3/14; all four floating orifices deployed since 3/24.

All required STSs were installed in working MUs before the 1 April deadline.

Maintenance:

JD Structural raked all the MU intake trashracks before 1 April as required by FPP. Debris abundance has been increasing later in the week.

JD North AWS pumps - four out of total six are available and in service. AWS pumps # 2 and 4 continue in OOS status due to RTDs and lower bearing issues. JD Engineering working with the pumps' contractor on bringing those pumps to service soon.

JD Mechanical/ Structural crews completed minor repair (design issue - Ms. Richards, PM) of the JD North entrance weir on 3/25. Great support work !

Calibration: 3/7/2014 NE1, NE2 were off by more than 0.3' ; a trouble report was written. All other water sensors were within the criteria of 0.3' .

Research:

JD Fisheries coordinating with research groups for the upcoming 2014 studies:

PSMFC/WDFW dam angling for the pikeminnow will occur from the JD tailrace deck same as in the last few years.

Oregon DFW pikeminnow crew will survey JD Forebay BRZ (Oregon side) with electroshocking boat in May. BRZ entry permit is pending.

U of I Testing of JD North LPS (Lamprey Passage System) preparing for their passage season's work starting in June 2014.

Battelle's Monitoring of Juvenile Salmonids with Hydroacoustic Tags completed installation of all JD Powerhouse and Spillway hydrophones in February.

2014 Adult Salmonids counting started at both JD Fishways by the Normandeau crew on 1 April as required by FPP.

Adult Salmonids Radio telemetry evaluations are ongoing at both JD adult fishway. University of Idaho crew is in charge of detecting of all adult adult salmonids, which were tagged and released at Bonneville Dam.

Glen A. Smith PE

Date: ___ 9-Apr-14

OPM John Day/Willow Creek Project

2007-2013 Water Temps JDA w/ 12yr avg



JDA COLLECTION CHANNEL VELOCITY


Date 29-Mar-14

By: pk

Bay(s)	Time	Sec.	Velocity (f/s)
0-2	0:01:14	74	2.17
2 - 4	0:02:02	122	3.16
4 - 6	0:02:53	173	3.21
6 - 8	0:03:50	230	3.10
8 - 10	0:04:43	283	3.21
10 - 12	0:05:34	334	3.00
12 - 14	0:06:31	391	2.69
14 - 16	0:07:29	449	3.21
16 - 18	0:08:08	488	4.29


3.12

Bird Count by Activity

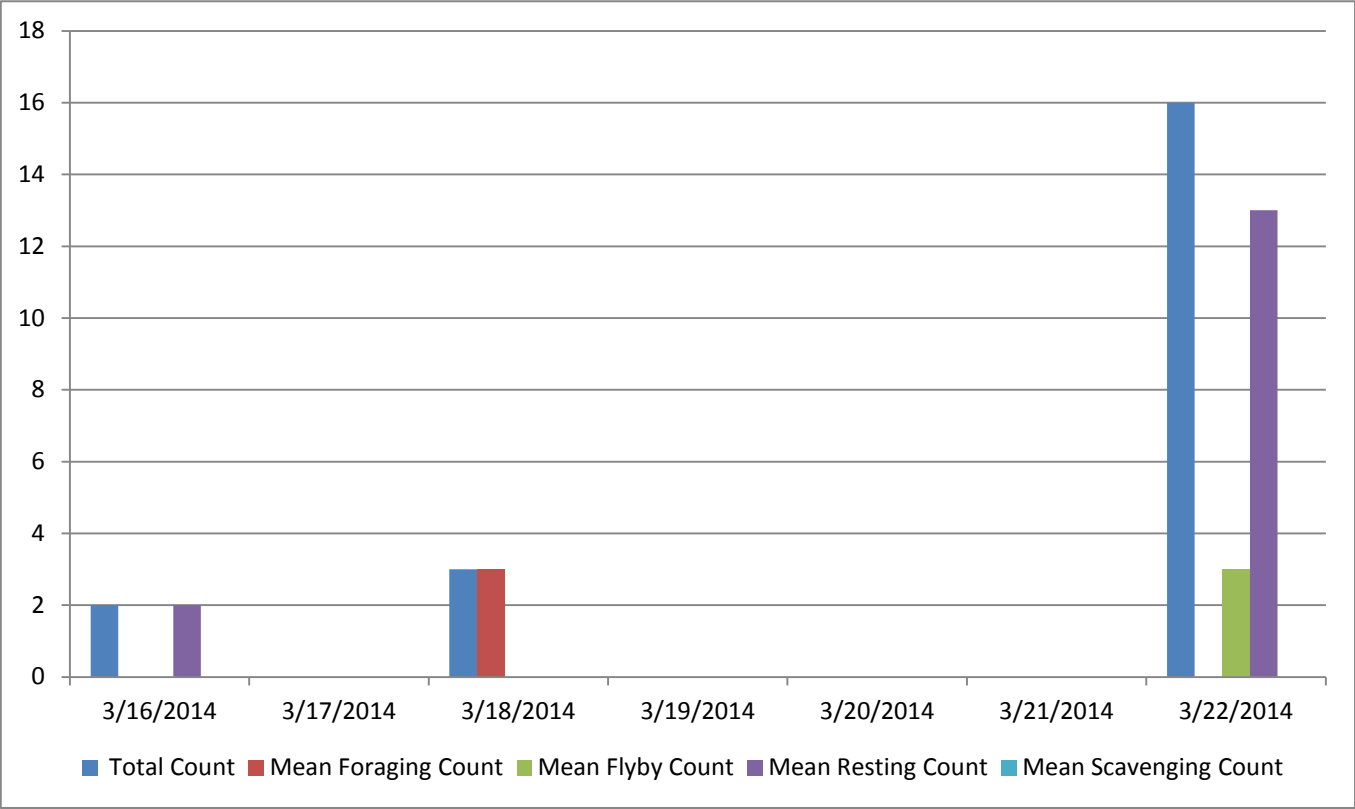

Date	Total Count	Mean Foraging Count	Mean Flyby Count	Mean Resting Count	Mean Scavenging Count
3/16/2014	2	0		2	
3/17/2014	0	0			
3/18/2014	3	3	0		
3/19/2014	0		0	0	
3/20/2014	0	0	0	0	
3/21/2014	0	0	0	0	
3/22/2014	16	0	3	13	

John Day Dam
Avian Zones 2013

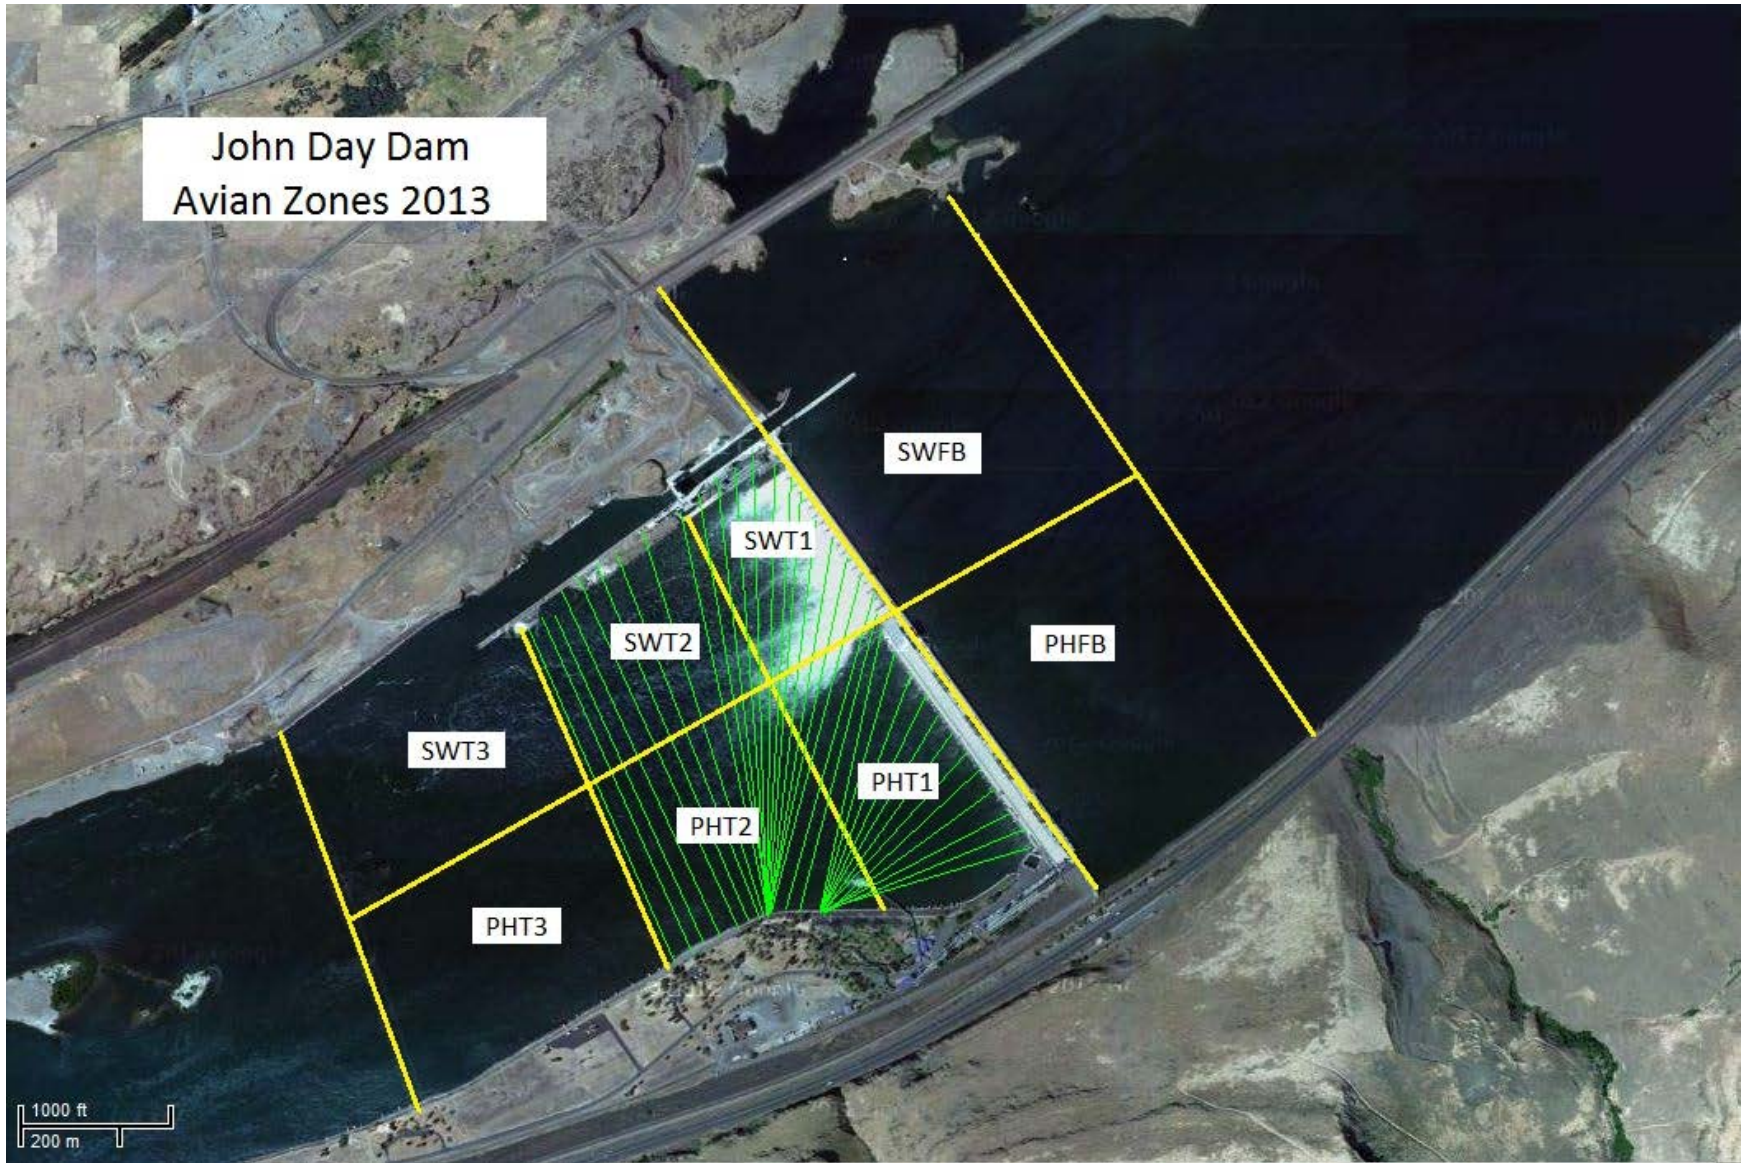

John Day:

	Temp:	Secchi:	Fallbacks
Sun	43	2.0	0
Mon	44	3.0	
Tues	44	3.5	
Wed	44	2.0	
Thur	43	2.0	
Fri	43	3.0	
Sat	43	3.0	
AVG:	43	AVG: 2.6	AVG 0
			MAX 0
			MIN 0

	NE1	NE2	S.Ent	SE1	N.Ent	JBS Diff	Bay1	Bay19
Sun	12.1	11.9	1.6	8.9	1.4	4.5	1.9	1.6
Sun	11.0	10.9	1.4	8.0	1.6	4.3	1.7	1.7
Mon	12.1	11.9	1.3	8.9	1.6	4.4	1.6	1.4
Mon	11.0	11.0	1.4	8.2	1.6	4.4	1.8	1.7
Tues	10.7	10.6	1.6	8.0	oos	4.9	1.9	1.8
Tues	11.2	11.1	1.4	8.2	oos	oos	1.6	1.5
Wed	12.3	12.1	1.0	8.7	1.5	4.4	1.5	1.1
Wed	9.9	10.0	1.0	8.7	1.5	4.5	1.6	1.7
Thur	10.3	10.3	1.3	9.0	1.5	4.8	1.6	1.5
Thur	9.5	9.5	1.5	8.1	1.4	4.5	1.9	1.8
Fri	11.6	11.4	1.1	9.6	1.5	4.6	1.5	1.4
Fri	10.6	10.4	1.4	8.6	1.5	4.6	1.7	1.6
Sat	10.6	10.5	1.2	8.5	1.4	4.6	1.5	1.5
Sat	11.5	11.3	1.3	9.2	1.4	4.6	1.7	1.6
AVG:	11.0	10.9	1.3	8.6	1.5	4.5	1.7	1.6
