

The Dalles Dam Fishway Status Report

January 6th, 2018

Inspection Period: Dec. 30 - Jan. 05, 2019

THE DALLES DAM



US Army Corps
of Engineers
Portland District

The Dalles Project-Fisheries
P.O. Box 564
The Dalles, OR 97058-9998
Phone: 541-506-3800

The Dalles Dam	Inspections Out of Criteria	Criteria Limit	Total Number of Inspections: Comments: FU's off 12/1 for dewatering	Temperature: 43.5 °F Secchi: 5+ feet
NORTH FISHWAY				
Exit differential	0	≤ 0.5'		
Count station differential	0	≤ 0.3'		
Weir crest depth	0	1.0' ± 0.1'		
Entrance differential	0	1.0' - 2.0'	1.4	
Entrance weir N1	0	depth (≥ 8')	10.6	
Entrance weir N2	0	Closed		
PUD Intake differential	0	≤ 0.5'		
EAST FISHWAY - Dewatered for annual maintenance				
Exit differential		≤ 0.5'		
Removable weirs 154-157		Per forebay		
Weir 158-159 differential		1.0' ± 0.1'		
Count station differential		≤ 0.3'		
153 Weir crest depth		1.1' ± 0.1'		
Junction pool weir JP6		0.0		
East entrance differential		1.0' - 2.0'		
Entrance weir E1		No criteria		
Entrance weir E2		depth (≥ 8')		
Entrance weir E3		depth (≥ 8')		
Collection channel velocity		1.5 - 4 fps		
Transportation channel velocity		1.5 - 4 fps		
North channel velocity		1.5 - 4 fps		
South channel velocity		1.5 - 4 fps		
West entrance differential		1.0' - 2.0'		
Entrance weir W1		depth (≥ 8')		
Entrance weir W2		depth (≥ 8')		
Entrance weir W3		No criteria		
South entrance differential		1.0' - 2.0'		
Entrance weir S1		depth (≥ 8')		
Entrance weir S2		depth (≥ 8')		
JUVENILE PASSAGE				
Sluiceway operation	0	Units 1, 18	MU1 (1-1) & MU18 (18-3) endgate closed	
Turbine trashrack drawdown	0	<1.5', biwklly		
Spill volume/pattern	0	None		
Turbine Unit Priority	0	per FPP	Bus maintenance work	
Turbine 1% Efficiency	0	per FPP		

OTHER ISSUES:

Predators;

Eagle numbers increasing in westrick park.
No Sea Lion observations

Operation:

East fish ladder dewatered. RTS 1/17/19
North ladder in service. To be dewatered 1/22/19

Current Outages;

FU1 and FU2 OOS for annual/overhaul maintenance and breaker replace. RTS 1/31/19
MU1 and MU2 (T1 transformer) OOS for FU breaker replace. RTS 1/9/19
MU5 forced OOS blade seals and T3 transformer replace. RTS 3/21/2019
MU6 OOS annual and T3 transformer replace. RTS 3/21/2019
MU12 FOOS through 1700 1/17/2019 for Blade Seals
MU16 OOS exciter replacement. RTS 3/28/2019
MU19 and MU20 forced OOS transformer acetylene production. RTS 10/24/2019


Maintenance

East count station window brush replaced.
Count station reflooring and electrical upgrade start soon.
Collection channel dewatering pumps 3 and 4 installed.
Assembly start on fishway automation replacement. Start install winter of 2019/20
East ladder exit weirs 156 and 157 removed. Wheels replaced. Awaiting install.
Diffuser valve status evaluation continues. Planning underway for rehab. In FPOM review.
Vegetation removal from south channel rock walls complete. Goats to remove vegetation on top side. North ladder vegetation removal after 1/22/19
Fish related /non-fish funded items; Spillway assessment underway. Spillway crane replace and spillgate 9 repair included.
All spillway items on Critical Infrastructure. Spillgate 9 on large cap list, projected for 2022. Comprehensive spillway assessment review underway.

Research/Construction/Contractors:

Bathymetry of spillwall and spill basin completed. District dive/ROV personnel inspected spill basin w/ ROV unit (12/11), awaiting results
Zebra mussel veliger sampling resumes next spring.
Lower Columbia River Forebay Temperature Monitoring completed. Equipment removed. To resume next spring.
AWS construction - Commissioning test and operation with single fish unit test completed. Follow on construction items identified.
PSMFC weekly sampling completed for the North Wasco County PUD's. New sample collection tank installation postponed to winter 2019/20.
PITAGS North and east fishladder data collection at count stations continues. Will maintain equipment during dewatering.
Fish Counters - Likely start with video 4/1/19 until contractor issues resolved. Fish Field Unit to provide support.
Pikeminnow dam angling - Caught 1785 YTD. Fishing resumes next spring. Debate over bass and walleye catch and release continues.
ODFW monthly fishway inspections concluded 10/16. Awaiting annual report.
Lamprey minor mods - Rounded entrance weir caps installed south, west, north entrances. East weirs completed. Guide blocker added to reduce pinch mortalities.
Univ of Idaho lamprey radiotelemetry completed. New antenna mounts at east, west and south installed Jan 2. Lamprey passage test to resume in May.
Lamprey trapping by tribes completed for season. Awaiting final numbers. Project to construct single lift hoist mechanism for next trapping season.
Fish unit breaker replace - Prep work in progress. Installation 12/1/18 - 1/14/19.
Fish unit rehab - Test of AWS backup with single fish unit complete. Will affect rehab alternative selection.
Transformer replacement - Install T3 underway (units 5 and 6). Sequence schedule modified from original

Approved by: Bryan Hert acting for Ron Twiner
Operation Project Manager The Dalles Dam

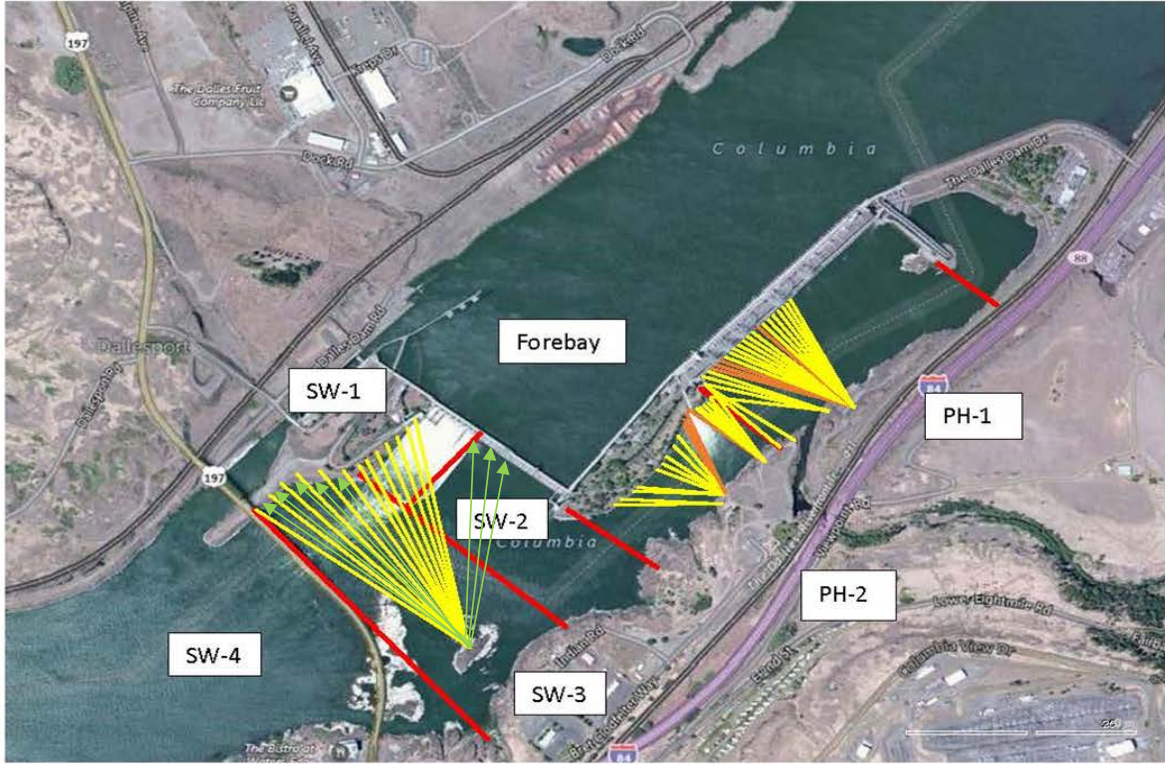

Red lines = avian zones

Yellow lines = current wires

Orange lines = down or missing wires



Additional avian lines installed 9/2018

2018 Piscivorous Bird Counts


F=foraging, NF=non-foraging

Date	Observer	AM/PM	Zone	Gull		Cormorant		Caspian tern		Grebe		Pelican		Other		Total birds in zone	Notes		
				F	NF	F	NF	F	NF	F	NF	F	NF	F	NF				
12/30	JED	AM	FB	5	0	6	0	0	0	0	0	0	0	0	1	0	12	BAEA BAEA Sunny, 40F, 20mph COME	
			PH1	8	14	4	4	0	0	0	0	0	0	0	0	0	0		30
			PH2	0	0	0	0	0	0	0	0	0	0	0	0	2	0		2
			SW1	0	51	0	0	0	0	0	0	0	0	0	0	0	0		51
			SW2	0	0	0	0	0	0	0	0	0	0	0	0	0	0		0
			SW3	0	205	0	95	0	0	0	0	0	0	0	0	7	0		307
12/31	BC	AM	FB	0	0	8	0	0	0	1	0	0	0	0	0	0	9	COME BAEA	
			PH1	0	0	0	5	0	0	0	0	0	0	0	0	8	13		
			PH2	0	0	0	0	0	0	0	0	0	0	0	8	0	8		
			SW1	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
			SW2	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
			SW3	0	8	0	55	0	0	0	0	0	0	0	0	0	0		63
1/1	JWR	PM	FB	0	0	10	0	0	0	3	0	0	0	0	5	18	4 BAEA, 1 GBHE 25 COME F, 1 BAEA NF, 1 GBHE NF 13 BAEA, 5 GBHE COME		
			PH1	9	0	0	0	0	0	0	0	0	0	25	2	36			
			PH2	0	0	0	0	0	0	0	0	0	0	0	18	18			
			SW1	0	0	0	0	0	0	0	0	0	0	1	0	1			
			SW2	0	0	0	0	0	0	0	0	0	0	0	0	0			
			SW3	0	65	1	86	0	0	0	0	0	0	0	0	0		152	
1/2	JWR	AM	FB	0	6	13	0	0	0	0	0	0	0	0	4	23	BAEA COME BAEA BAEA		
			PH1	14	44	0	18	0	0	0	0	0	0	5	8	89			
			PH2	0	0	0	0	0	0	0	0	0	0	0	16	16			
			SW1	0	0	1	0	0	0	0	0	0	0	0	6	7			
			SW2	0	0	0	0	0	0	0	0	0	0	0	0	0			
			SW3	0	0	3	29	0	0	0	0	0	0	0	0	0		32	
1/3	JWR	AM	FB	0	3	0	8	0	0	1	0	0	0	0	1	13	BAEA COME BAEA BAEA		
			PH1	0	0	0	0	0	0	0	0	0	0	12	8	20			
			PH2	0	0	0	0	0	0	0	0	0	0	0	13	13			
			SW1	0	0	0	0	0	0	0	0	0	0	0	5	5			
			SW2	0	0	0	0	0	0	0	0	0	0	0	0	0			
			SW3	0	0	4	25	0	0	0	0	0	0	0	0	0		29	
1/4	JWR	AM	FB	0	0	3	0	0	0	1	0	0	0	0	3	7	Grebe = pied-billed; Other = BAEA in towers all east; other = 4 COME F, 1 COME NF, 1 BAEA NF BAEA		
			PH1	4	0	0	0	0	0	0	0	0	0	4	2	10			
			PH2	0	0	0	0	0	0	0	0	0	0	0	9	9			
			SW1	0	0	0	0	0	0	0	0	0	0	0	0	0			
			SW2	0	0	0	0	0	0	0	0	0	0	0	0	0			
			SW3	0	2	0	55	0	0	0	0	0	0	0	0	0		57	
1/5	JWR	AM	FB	0	10	12	0	0	0	1	0	0	0	5	28	BAEA BAEA BAEA BAEA			
			PH1	13	43	0	4	0	0	0	0	0	0	0	2		62		
			PH2	0	0	0	0	0	0	0	0	0	0	0	15		15		
			SW1	0	0	0	0	0	0	0	0	0	0	0	5		5		
			SW2	0	0	0	0	0	0	0	0	0	0	0	0		0		
			SW3	0	17	0	24	0	0	0	0	0	0	0	0		0	41	
SW4	0	165	0	0	0	0	0	0	0	0	0	0	0	165					

Key: BAEA = Bald Eagle; GBHE = Great Blue Heron; COME = Common Merganser

The Dalles Dam River Temperatures

—●— Current USGS Daily Average —▲— USGS Daily Average (2007-2017)

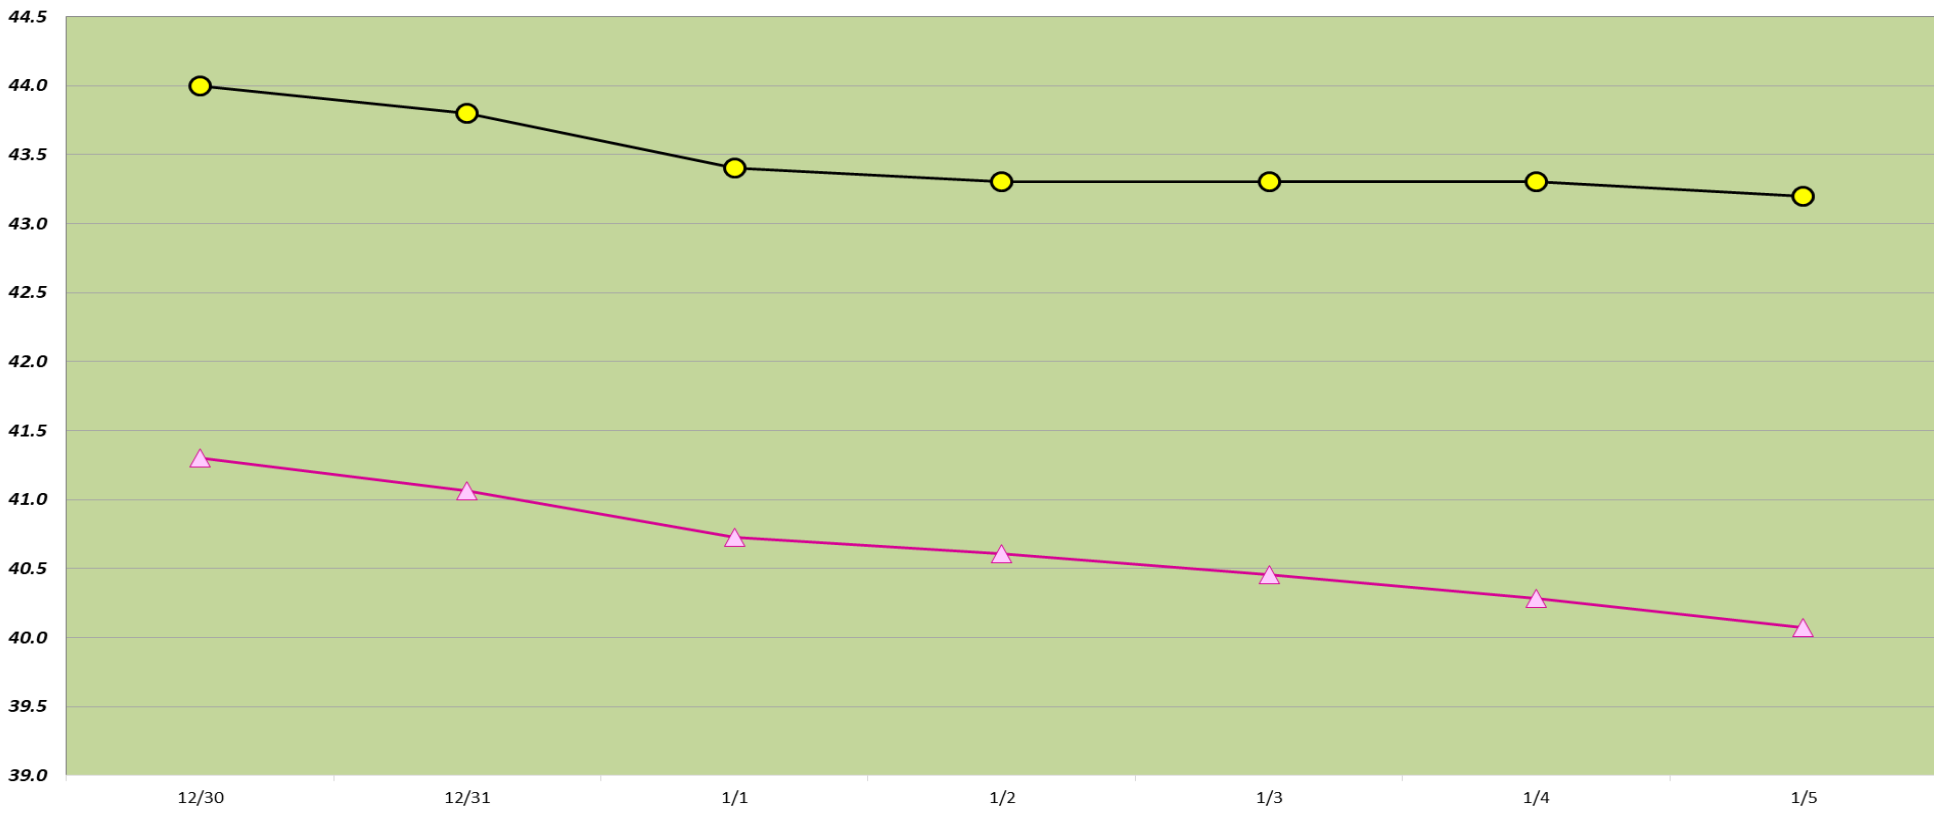

	Secchi:		USGS: Temperatures
12/30	5+	Sun	44.0
12/31	5+	Mon	43.8
1/1	5+	Tue	43.4
1/2	5+	Wed	43.3
1/3	5+	Thurs	43.3
1/4	5+	Fri	43.3
1/5	5+	Sat	43.2
	5+	AVG	43.5

**The Dalles Dam Daily Readings and Averages for
Temperatures, Secchi, Entrances, and Spill**

SCADA INSPECTION
= Out of criteria

Date:	North Ladder			East Ladder										
	North Entrance		East Entrance					West Entrance				South Entrance		
	Differential	N1 Depth	Differential	E1 Depth	E2 Depth	E3 Depth	JP 6	Differential	W1 Depth	W2 Depth	W3 Depth	Differential	S1 Depth	S2 Depth
12/30	1.3	10.5												
12/31	1.3	10.5												
1/1	1.4	10.5												
1/2	1.4	10.6												
1/3	1.4	10.6												
1/4	1.3	10.7												
1/5	1.4	10.5												
AVG:	1.4	10.6												

Ladder dewatered for maintainence RTS 01/20/2019

Fishways are inspected twice daily plus one SCADA inspection.
