The Dalles Dam Fishway Status Report

5/23/2021

Inspection Period: 5/16-5/22

THE DALLES DAM



The Dalles Project-Fisheries P.O. Box 564 The Dalles, OR 97058-9998 Phone: 541-506-3800

The Dalles Dam	Inspections	Criteria	Total Number of Ins		Temperature: 57.3 °F	
THE Dailes Daili	OOC	Limit	Comments:	AWS operating well.	Weekly Ave. Secchi:	4.7
			NORTH F	ISHWAY		
Exit differential	0	≤ 0.5'				
Count station differential	0	≤ 0.3'				
Weir crest depth	0	1.0' ± 0.1'				
Entrance weir N1	0		Weekly average	10.2		
Entrance Differential	0		Weekly average	1.3		
Entrance weir N2	0	Closed				
PUD Intake differential	0	≤ 0.5'				
			EAST FIS	SHWAY		
Exit differential	0	≤ 0.5'				
Removable weirs 154-157	0	Per forebay				
Weir 158-159 differential	0	1.1' ± 0.1'				
Count station differential	0	≤ 0.3'				
153 Weir crest depth	0	1.0' ± 0.1'				
Junction pool weir JP6	0	> 7.0'				
East entrance differential	0	1.0' - 2.0'	1 fish unit operation	Week ave. 1.5		
Entrance weir E1	0	No criteria				
Entrance weir E2	0	depth (≥ 8')		Week ave. 10.5		
Entrance weir E3	0	depth (≥ 8')		Week ave. 10.2		
Collection channel velocity	0	1.5 - 4 fps	2.48 fps 5/12/21	Range MU15 1.95- MU20 3.07 fp	os .	
Transportation channel velocity	0	1.5 - 4 fps	2.46 fps 5/12/2021			
North channel velocity	0	1.5 - 4 fps	2.44 fps, 5/12/2021			
South channel velocity	0	1.5 - 4 fps	2.81 fps 5/12/21			
West entrance differential	0	1.0' - 2.0'	Old SCADA	Week ave. 1.6		
Entrance weir W1	0	depth (≥ 8')		Week ave. 10.4		
Entrance weir W2	0	depth (≥ 8')		Week ave. 10.4		
Entrance weir W3	0	No criteria	Closed			
South entrance differential	0	1.0' - 2.0'		Week ave. 1.4		
Entrance weir S1	0	depth (≥ 8')	1 fish unit operation	Week ave. 10.2		
Entrance weir S2	0	depth (≥ 8')	1 fish unit operation	Week ave. 9.2		
			JUVENILE F	PASSAGE		
Sluicegate operation	0	Units 1, 18	Gates over MU1/1-2-	-3,MU8/1-3,MU18-2 open		
Turbine trashrack drawdown	0			within drawdown criteria.		
Spill volume/pattern	0	1 to 8	Spilling 8 gates.			
Turbine Unit Priority	0	per FPP				
Gatewells	0	Weekly	No mortality. Decrea	asing #s of salmon fry and smolts	in gatewells, 5/12/2021	

OTHER ISSUES:

Current Unit Outages

MU12 OOS 0001 4/12/2021 - 1700 10/27/2022 for Annual & Cooler Upgrades

T10 (MU19 and 20) OOS 10/27/22 acetylene levels

MU22 out 3/1/2021 – 5/20/2021 for Top Plate Cover Upgrades

FU1 FOOS through 5/21/2021 due to a ground fault on FSJ2

Maintenance

PUD intake rake returned to service with temporary power. Exploring permanent options.

Five of 6 east fishway collection channel dewatering pumps removed for repair/rehab. Work to resume in July.

Fishway automation replacement on hold from lack of staff. East exit, east and south entrances complete. West and north operating with old system.

Calibrations for east entrance weir E3 lower than actual opening. All in criteria >8'. Maintenance notified.

AWS backup system closed just prior to return to fish unit 1. Intake differential increased requiring a second closure cycle to clear. Visible milfoil floated off.

Spillway assessment (MRER); Spillgates 1- 9 rehab date estimate 2034. Includes replacement of spillbay 9 trunnion pin repair

Predators

Heron numbers increasing (up to 8) inside east fishladder Finding Shad morts atop weirs. Doing frequent ladder walks and USDA hazing when they can.

Cormorants feeding at east fishway exit. Hazing when we can.

High gull numbers with aggressive foraging below spillway in SW3 and 4. High cormorant nest numbers (50-60) on BPA towers.

No opportunity for Green laser use for piscivorous bird hazing testing.

Pikeminnow dam angling ongoing. Removing native pikeminnow, yet All invasive bass/walleye by-catch continue to be RELEASED per state requirement.

Processing PIT tag data recovered. Camera monitoring within fishway for possible avian predators.

Research/Construction/Contractors

Fish counters started Apr1. No issues.

AWS intake trashrack - EDR funded for FY21 to investigate solution for debris plugging issue. PDT meetings in progress.

PITAGS north and east fishladder data collection at count stations continues.

Fish unit rehab - Phase 1A on hold. Planning operation with AWS backup water supply during construction.

Fishway Operations

Ice Trash sluiceway opened 24/7. MU1/1-2-3, MU 8/1-3, MU18/2


East and north fishladders in full operation per Fish Passage Plan.

New automation installed at east exit, east entrance and south entrane working well with minor adjustments.

Spillway open at 40% river flow


Approved by: Ron Twiner, Operation Project Manager, The Dalles Dam

New Avian Lines and laser deterrent zones

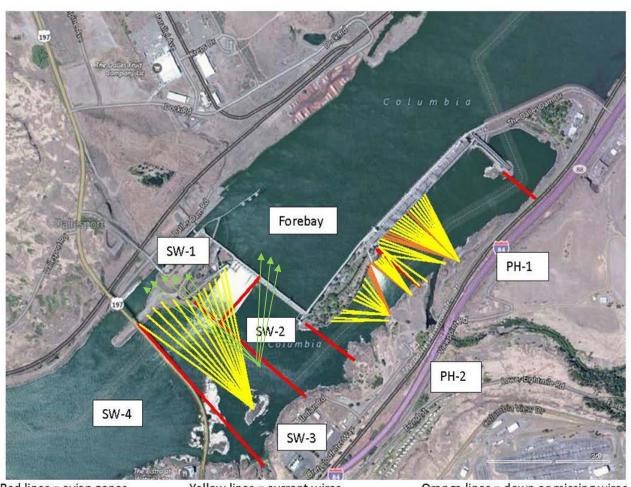



				Gull F	Gull NF	Corm F	Corm NF
5/16			FB	0	0	2	54
5/16			PH1	0	0	0	0
5/16			PH2	0	0	0	0
5/16	JWR	AM	SW1	0	0	0	0
5/16			SW2	0	0	0	0
5/16			SW3	8	0	0	0
5/16			SW4	34	24	0	0
5/17			FB	0	0	0	0
5/17			PH1	0	0	0	0
5/17			PH2	0	0	0	0
5/17	JWR	PM	SW1	0	0	0	0
5/17			SW2	0	0	0	0
5/17			SW3	0	0	0	0
5/17			SW4	0	0	0	0
5/18			FB	0	0	0	0
5/18			PH1	0	0	0	0
5/18			PH2	0	0	0	0
5/18		AM	SW1	0	0	0	0
5/18			SW2	0	0	0	0
5/18			SW3	0	0	0	0
5/18			SW4	0	0	0	0
5/19			FB	5	8	0	112
5/19			PH1	0	0	0	0
5/19			PH2	0	0	0	0
5/19	JED	PM	SW1	0	0	0	0
5/19			SW2	0	0	0	0
5/19			SW3	15	135	2	0
5/19			SW4	85	215	0	0
5/20			FB	0	0	2	88
5/20			PH1	0	0	1	2
5/20			PH2	0	0	0	0
5/20	JED	AM	SW1	0	0	0	0
5/20			SW2	2	0	0	0
5/20			SW3	15	165	2	7
5/20			SW4	170	110	2	0
5/21			FB	0	5	2	75
5/21			PH1	0	0	1	6
5/21			PH2	1	0	1	0
5/21	JED	PM	SW1	0	0	0	0
5/21			SW2	2	0	1	0
5/21			SW3	20	145	2	9
5/21			SW4	50	100	2	20
5/22			FB	5	0	0	65
5/22			PH1	0	0	1	0
5/22			PH2	3	0	0	0
5/22	JED	AM	SW1	12	0	0	0
5/22			SW2	2	0	0	0
5/22			SW3	80	30	5	0
5/22			SW4	160	50	4	15

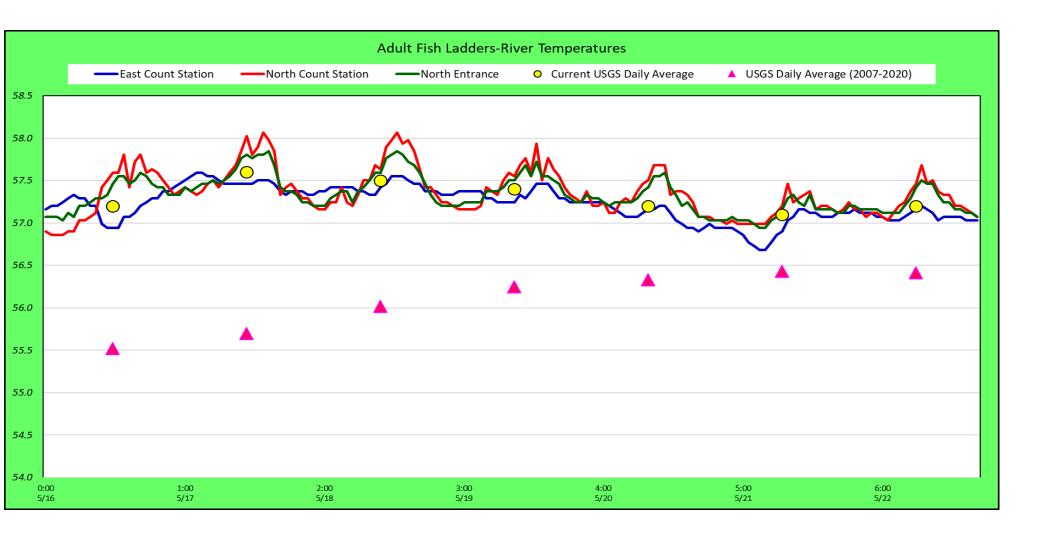

_				_
	Secchi:		°F	USGS May
5/16	5.0	Sun	57.2	
5/17	5.0	Mon	57.6	
5/18	5.0	Tue	57.5	
5/19	5.0	Wed	57.4	
5/20	4.0	Thurs	57.2	
5/21	4.0	Fri	57.1	
5/22	5.0	Sat	57.2	
	4.7	AVG	57.3	

The Dalles Dam Daily Readings and Averages for

Temperatures, Secchi, Entrances, and Spill

E1 and W3 do not have criteria opening.
E3 value 1' '~ more than actual.
out of criteria

	North Ladder		East Ladder											
Date:			East Entrance				West Entrance			South Entrance				
	Differential	N1 Depth	Differential	E1 Depth	E2 Depth	E3 Depth	JP 6	Differential	W1	W2	W3	Differential	S1	S2
5/16	1.3	10.0	1.4	8.3	10.3	9.3	13.4	1.5	9.1	9.1	-0.3	1.2	10.2	9.0
	1.3	10.1	1.4	8.4	10.3	9.3	13.4	1.5	9.1	9.1	-0.3	1.2	10.3	9.2
5/17	1.3	10.2	1.5	8.2	10.2	9.2	13.2	1.5	9.1	9.1	-0.4	1.2	10.1	8.8
	1.3	10.2	1.5	8.3	10.3	9.3	13.3	1.5	9.1	9.1	-1.4	1.2	10.2	8.9
=/40	_							_						
5/18	1.3	10.1	1.5	8.3	9.6	8.7	13.2	1.6	9.0	9.0	-0.6	1.3	10.1	8.8
	1.3	10.2	1.4	8.5	9.9	8.9	13.5	1.6	9.6	9.1	-0.3	1.2	10.4	9.0
E/40							10.0							
5/19	1.3	10.3	1.4	8.2	9.2	9.2	13.2	1.6	9.0	9.0	-0.6	1.2	10.4	9.0
	1.4	10.1	1.3	8.4	9.4	9.3	13.4	1.7	11.0	11.0	-0.4	1.2	10.4	10.0
5/20	1.4	10.2	1.5	9.3	11.4	11.0	13.4	1.6 1.5	11.3	11.3 11.6	-0.8 -0.4	1.5	10.4	9.0
3/20	1.4	10.2	1.5	9.3	11.4 11.3	11.8 11.7	13.4	1.6	11.4 11.5	11.5	-0.4	1.7	10.4 10.2	8.9
	1.4	10.2	1.5	9.2	11.5	11.7	15.5	1.7	11.5	11.5	-0.5	1.7	10.2	0.9
5/21	1.3	10.2	1.5	9.3	11.5	11.9	13.4	1.6	11.6	11.6	-0.6	1.5	9.9	9.6
3/21	1.3	10.2	1.6	9.0	11.1	11.5	13.1	1.6	11.6	11.6	-0.5	1.5	10.8	9.6
	1.5	10.2	1.0	5.0	11.1	11.5	13.1	1.0	11.0	11.0	0.5	1.5	10.8	3.0
5/22	1.3	10.1	1.6	9.0	11.2	11.6	13.1	1.5	11.5	11.7	-0.6	1.5	9.7	9.3
-	1.3	10.2	1.5	9.0	11.1	11.5	13.1	1.5	11.6	11.6	-0.8	1.6	9.8	9.4
AVG:	1.3	10.2	1.5	8.7	10.5	10.2	13.3	1.6	10.4	10.4	-0.6	1.4	10.2	9.2

Fishways are inspected twice daily. Overnight trend monitored via Old SCADA.



AWS intake, floating off debris during close cycle
