ID	Task Name	Duration	Start	Finish
1	**DDR**	**120 days?**	**Mon 8/1/11**	**Fri 1/13/12**
2	**Weekly Meetings**	**106 days**	**Mon 8/1/11**	**Mon 12/26/11**
25	**Planning**	**10 days?**	**Mon 8/15/11**	**Fri 8/26/11**
26	kick off meeting	1 day	Fri 8/19/11	Fri 8/19/11
27	Budget estimates	5 days	Mon 8/15/11	Fri 8/19/11
28	Specs intact setup	1 day	Thu 8/18/11	Thu 8/18/11
29	Project in Projectwise	3 days?	Thu 8/18/11	Mon 8/22/11
30	Route SSB	5 days	Mon 8/22/11	Fri 8/26/11
31	**30% DDR**	**27 days**	**Mon 8/22/11**	**Tue 9/27/11**
32	Research and documentation	21 days	Mon 8/22/11	Mon 9/19/11
33	Site Visit	1 day	Thu 9/1/11	Thu 9/1/11
34	Prepare DDR Outline	14 days	Tue 8/30/11	Fri 9/16/11
35	In section review	3 days	Mon 9/19/11	Wed 9/21/11
36	Incorporate Comments	4 days	Thu 9/22/11	Tue 9/27/11
37	**60% DDR**	**38 days?**	**Wed 9/28/11**	**Fri 11/18/11**
38	Research and Documentation	19 days	Wed 9/28/11	Mon 10/24/11
39	Convert Outline to DDR Document	16 days	Mon 10/3/11	Mon 10/24/11
40	In section review	4 days	Tue 10/25/11	Fri 10/28/11
41	60 percent review	11 days?	Mon 10/31/11	Mon 11/14/11
42	Incorporate Comments	4 days	Tue 11/15/11	Fri 11/18/11
43	**90% DDR**	**40 days**	**Mon 11/21/11**	**Fri 1/13/12**
44	Design and documentation	16 days	Mon 11/21/11	Mon 12/12/11
45	Finishing Document	17 days	Fri 11/25/11	Mon 12/19/11
46	In section review	4 days	Tue 12/20/11	Fri 12/23/11
47	60 percent review	11 days	Mon 12/26/11	Mon 1/9/12
48	Incorporate Comments	4 days	Tue 1/10/12	Fri 1/13/12
49				
50	**Plans and Specifications**	**113 days**	**Mon 1/16/12**	**Wed 6/20/12**
51	**P&S Meetings**	**111 days**	**Wed 1/18/12**	**Wed 6/20/12**
64	**Planning**	**10 days**	**Mon 1/16/12**	**Fri 1/27/12**
65	Kickoff meeting	1 day	Mon 1/16/12	Mon 1/16/12
66	Budget Estimates(if needed)	3 days	Wed 1/18/12	Fri 1/20/12
67	Identify ATR lead	5 days	Mon 1/23/12	Fri 1/27/12
68	Projectwise Changes	2 days	Thu 1/26/12	Fri 1/27/12
69	Site Visit Confirm Recommended actions	1 day	Tue 1/24/12	Tue 1/24/12
70	**Design to 60%**	**53 days**	**Mon 1/30/12**	**Wed 4/11/12**
71	Design effort	30 days	Mon 1/30/12	Fri 3/9/12
72	Prepare drawing list	2 days	Mon 1/30/12	Tue 1/31/12
73	Prepare Spec list	2 days	Wed 2/1/12	Thu 2/2/12
74	List design coordination issues	3 days	Thu 2/23/12	Mon 2/27/12
75	In section review(Peer)	3 days	Mon 3/12/12	Wed 3/14/12
76	In section Review (Supr)	3 days	Thu 3/15/12	Mon 3/19/12
77	Assemble 60% Review Package	1 day	Tue 3/20/12	Tue 3/20/12
78	Post 60% review Package	1 day	Wed 3/21/12	Wed 3/21/12
79	60% review package	15 days	Thu 3/22/12	Wed 4/11/12
80				
81	**Design to 90 %**	**30 days**	**Thu 4/12/12**	**Wed 5/23/12**
82	Design Effort	30 days	Thu 4/12/12	Wed 5/23/12
83	In section review(Peer)	3 days	Thu 4/12/12	Mon 4/16/12
84	In section Review (Supr)	3 days	Tue 4/17/12	Thu 4/19/12
85	Assemble 90% Review Package	1 day	Fri 4/20/12	Fri 4/20/12
86	Post 90% review Package	1 day	Mon 4/23/12	Mon 4/23/12
87	90% review package	10 days	Tue 4/24/12	Mon 5/7/12
88	**BCOE**	**26 days**	**Tue 5/8/12**	**Tue 6/12/12**
89	BCOE revisons	14 days	Tue 5/8/12	Fri 5/25/12
90	In section review(Peer)	3 days	Tue 5/8/12	Thu 5/10/12
91	In section Review (Supr)	3 days	Fri 5/11/12	Tue 5/15/12
92	Assemble BCOE Package	1 day	Wed 5/16/12	Wed 5/16/12
93	Post BCOE review Package	1 day	Thu 5/17/12	Thu 5/17/12
94	BCOE review	11 days	Fri 5/18/12	Fri 6/1/12
95	Bcoe Backcheck	5 days	Tue 5/8/12	Mon 5/14/12
96	Final Revisions	5 days	Tue 5/8/12	Mon 5/14/12
97	Specs section advertise set	5 days	Tue 5/8/12	Mon 5/14/12
98	ATR	21 days	Tue 5/15/12	Tue 6/12/12
99	**Advertise and Award**	**69 days**	**Wed 6/13/12**	**Mon 9/17/12**
100	Route Check-Off List	3 days	Wed 6/13/12	Fri 6/15/12
101	Route coversheet	3 days	Mon 6/18/12	Wed 6/20/12
102	Contract Prep	4 days	Thu 6/21/12	Tue 6/26/12
103	Contracting and legal review	5 days	Wed 6/27/12	Tue 7/3/12
104	advertise	10 days	Wed 7/4/12	Tue 7/17/12
105	Pre-Bid Site Visit	1 day	Wed 7/18/12	Wed 7/18/12
106	EC-CC Prepares IGE	10 days	Thu 7/19/12	Wed 8/1/12
107	Reciept of Proposal	1 day	Thu 8/2/12	Thu 8/2/12
108	Negotiations	7 days	Fri 8/3/12	Mon 8/13/12
109	Legal Review/Issue award Notice	10 days	Tue 8/14/12	Mon 8/27/12
110	Contractor obtains bonds	10 days	Tue 8/28/12	Mon 9/10/12
111	NTP	5 days	Tue 9/11/12	Mon 9/17/12
112	**Contract Period**	**110 days**	**Tue 9/18/12**	**Mon 2/18/13**
113	Construction	90 days	Tue 9/18/12	Mon 1/21/13
114	Operational testing	10 days	Tue 1/22/13	Mon 2/4/13
115	Contract closeout	10 days	Tue 2/5/13	Mon 2/18/13

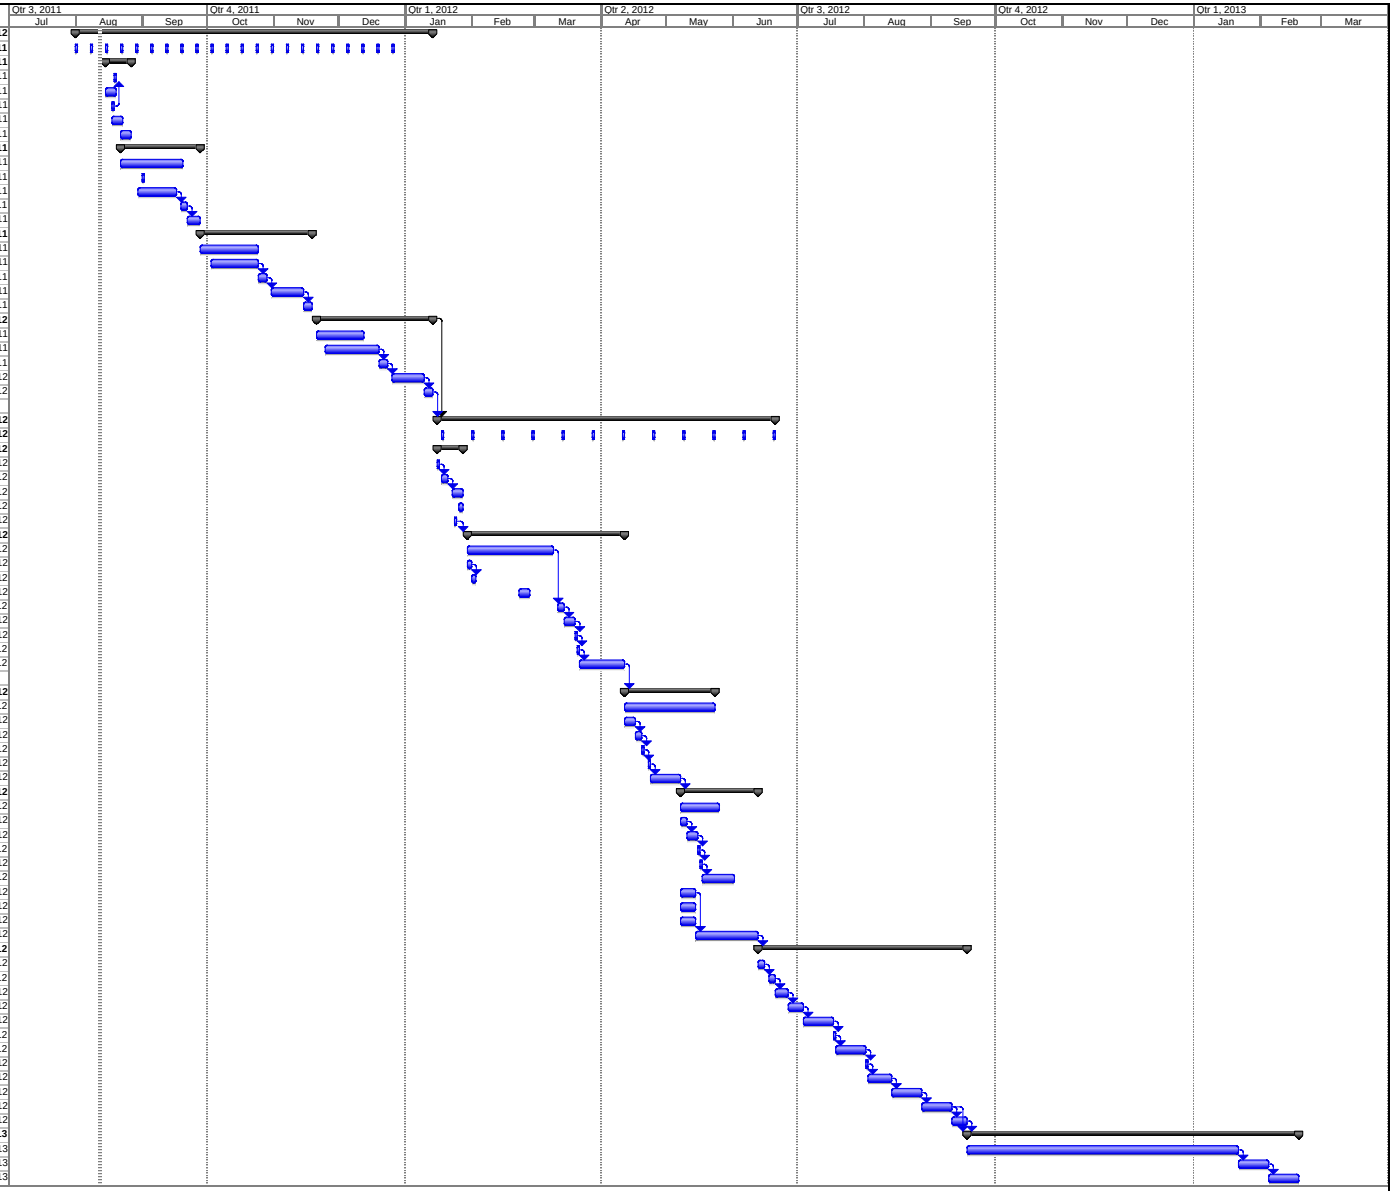

Project: B2 trash rake
Date: Fri 8/12/11

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
